

Hopewell Valley Regional School District
 Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS
 FVHD # 4924D

Progress Report #11- 12/23/17 to 1/19/18

Exterior Site Work:

E1. Building "B" Addition: Completed
 Concrete Slab



E2. Building "B" Addition: Completed
 Steel Erection "Phase 1" Columns & Beams



E3. Dumpster Enclosure- Underway
 Wall footings & Pad preparation.



E4. Building "B" Addition: Completed
 New Water line loop around new addition



Hopewell Valley Regional School District
 Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS
 FVHD # 4924D

- E5. Building "A" Addition: Completed
 Under slab Bathrooms Plumbing pipe installation



- E6. Building "A" Addition: Completed
 Prep for Radon piping installation and concrete



- E7. Building "A" Addition: Underway
 Underground Storm Line where existing Garage is thru Bulldogs walkway (remove existing pavers, memorial trees, plaques, install new pipe, new treatment devise, connect to existing inlet and replant ex. Trees in their existing locations)



Interior Work:

- 1 Classroom #118: Underway
 VCT floor installed- Prefab chase enclosure underway




Hopewell Valley Regional School District
 Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS
 FVHD # 4924D

- 2 300 Wing Toilets: Underway
 New piping roughing, pour concrete slab, chase wall framing, inspections, installing gypsum board, ceiling grid and prep for tile installation.



- 3 Classroom Swing #3 (312- 320): Underway
 Remove and replace existing ceiling tile, grid, HVAC duct grills, install new ceiling grid and new tiles.

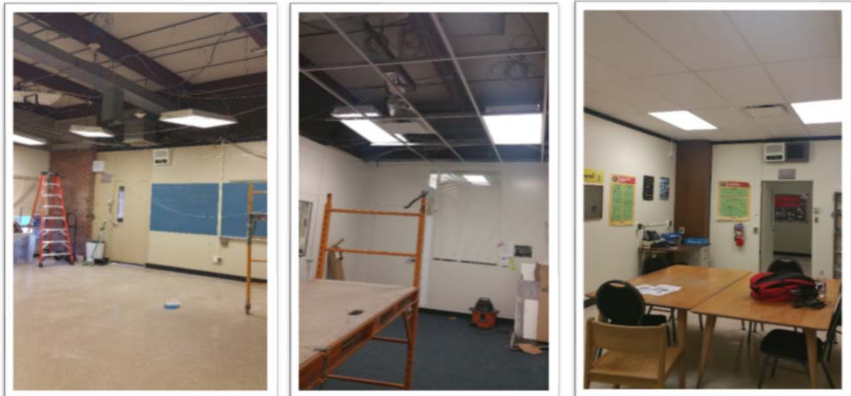

- 4 Boiler Room: Underway
 Install new pipes to bypass existing water storage tank

